WORKDAY HCM

User Adoption Metrics Dashboard

Role-based adoption intelligence for implementation teams.

Track what matters, for every audience, at every sprint.

HR professionals | Leadership | Managers | Employees

What this dashboard does

Context & framing

In a mandatory-use HCM environment, adoption is not about who shows up — it is about whether each audience is doing the right things for their role. This dashboard shifts the question from 'are users logging in?' to 'are users completing the tasks their role demands?'

Role overview

Traffic-light snapshot across all four audiences with scores and top-task completion at a glance.

Velocity tracking

Month-over-month trends showing whether adoption is accelerating, stalling, or declining per role.

Audience drilldowns

Per-role deep dives into workstreams, sub-group segmentation, and monthly heatmaps.

Action tracker

Open interventions with owners, due dates, and status — the bi-weekly sprint meeting agenda.

Role overview · adoption snapshot

73%	83%	18%	57%
Overall adoption	Tasks on time	Never attempted	Engagement elapsed

HR professionals

91%

Benefits admin	99%
Compliance rpt.	97%
Comp & merit	48%

Leadership

68%

Org dashboards	85%
Talent reviews	58%
Succession	38%

Managers

77%

Time approvals	94%
Job changes	52%
Succession	29%

Employees

62%

Time entry	89%
Personal info	44%
Career & learning	29%

Adoption velocity & close projection

Act 1 · Velocity

Implementation progress: week 8 of 14 (57% elapsed)

Go-live · Jan 6 | **Today · Wk 8 · 57%** | Close · Jul 18

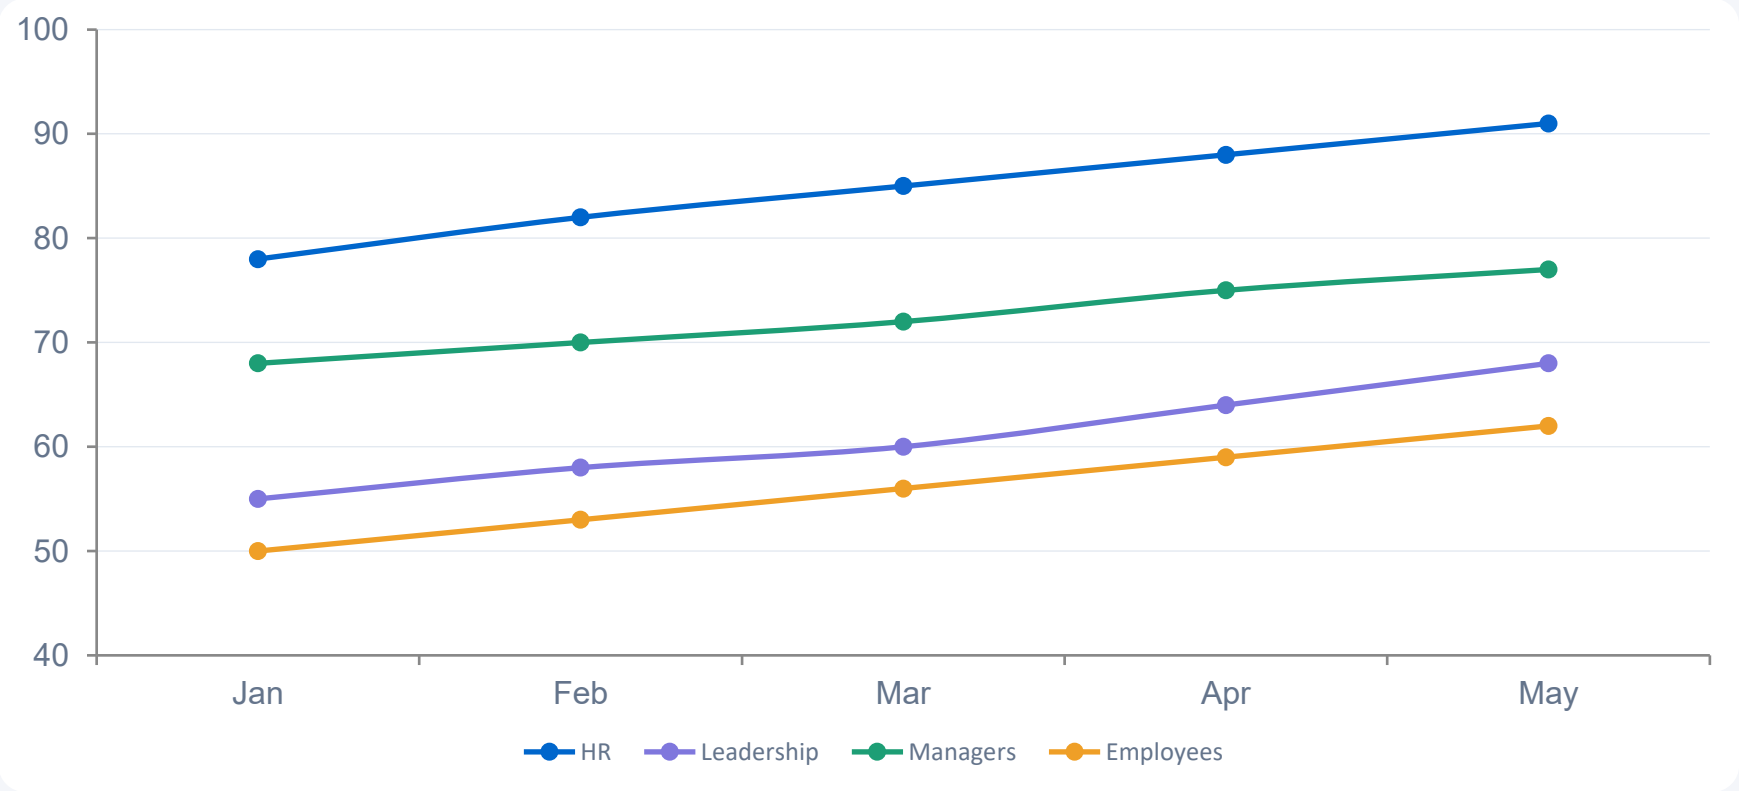

+6 pts/mo
Sprint velocity

6 weeks
Remaining

~84%
Projected at close

−1 pt
Gap to 85% target

HR professionals · adoption drilldown

142 users · 91% · Top performer

Act 2 · HR Focus

Workstream completion

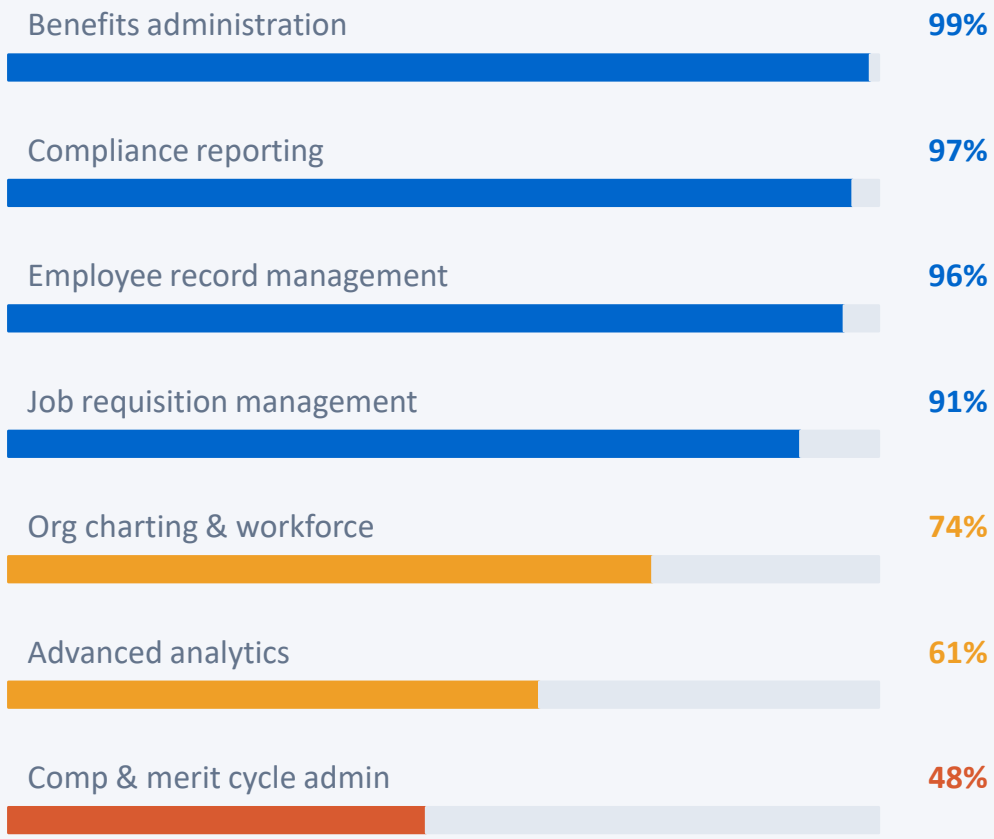

Key actions

- Comp & merit stalled at 48% — pre-cycle enablement session before next merit cycle (74 users)
- Advanced analytics at 61% but fastest-growing — office hours or peer champions to accelerate (55 users)
- L&D team scores 12 pts below HR peers — role-specific training paths recommended (20 users)
- No-HRIS background users closing gap — peer-pair with prior Workday users to compound gains (37 users)

Process efficiency impact vs. pre go-live

Benefits enrollment	14 days	→	**4 days**	↓ 71%
Compliance reporting	4 hrs	→	**12 min**	↓ 95%
Comp & merit cycle	21 days	→	**18 days**	↓ 14%

Managers · adoption drilldown

610 users · 77% · On track

Act 2 · Manager Focus

Workstream completion

Key actions

- Succession declining (↓3 pts/mo) — nudge campaign for 435 managers who've never opened this workstream
- Small-team managers (1–5 reports) lag large-team peers by 27 pts — task frequency is the root cause (200 users)
- Job change requests stalled flat — process or awareness gap, not usability; clarity session needed (293 users)
- New managers (<1 yr) score 58% — add Workday module to onboarding curriculum now (148 users)

Adoption by sub-group · selected highlights

Large teams (15+ reports)	88 %	Small teams (1–5 reports)	61 %
Operations dept.	91 %	Customer success dept.	53 %

Task completion · role × workstream heatmap

Act 2 · Cross-role view

Darker = higher completion rate. '—' = task not in scope for that role.

	HR	Leadership	Managers	Employees
Time & absence	96%	—	94%	89%
Benefits	99%	—	—	77%
Performance	88%	58%	74%	—
Reporting	94%	79%	68%	—
Comp & planning	82%	44%	52%	—
Career & learning	71%	38%	41%	29%
Profile & records	96%	—	—	44%

Scale: Low (<55%) · Mid (55–79%) · High (80–94%) · Excellent (95%+)

Open intervention tracker · all audiences

Act 3 · Open Actions

Standing agenda — reviewed and updated every bi-weekly sprint session

Action	Audience	Owner	Type	Due	Status
Comp & merit enablement session	HR	J. Patel	Training	Jun 6	In progress
Succession planning nudge campaign	Managers	S. Obi	Campaign	Jun 6	Not started
Small-team manager enablement	Managers	M. Lee	Coaching	Jun 13	Not started
Analytics office hours (HR)	HR	M. Lee	Coaching	Jun 13	Planned
Job change process clarity session	Managers	J. Patel	Workshop	Jun 20	Planned
New manager Workday onboarding mod.	Managers	S. Obi	Content	Jun 20	In progress
Peer-pair: prior Workday → no-HRIS	HR	J. Patel	Program	Jun 6	Complete

3 high priority · 3 medium · 1 opportunity · 1 complete · 2 in progress · 3 planned · 1 not started
